Release Forecast & Burn-up

Answer “when will it be done?” with a range, based on how fast the team actually finishes work.

Run a Project · Burn-up Chart · Throughput Forecasting · Ranges, Not Single Dates


WORKED EXAMPLE · FICTIONAL TEAM

RELEASE / SCOPE: Reorder made easy

FORECAST DATE: 13–20 June

1 Burn-up Chart

PLOT AFTER EVERY ITERATION

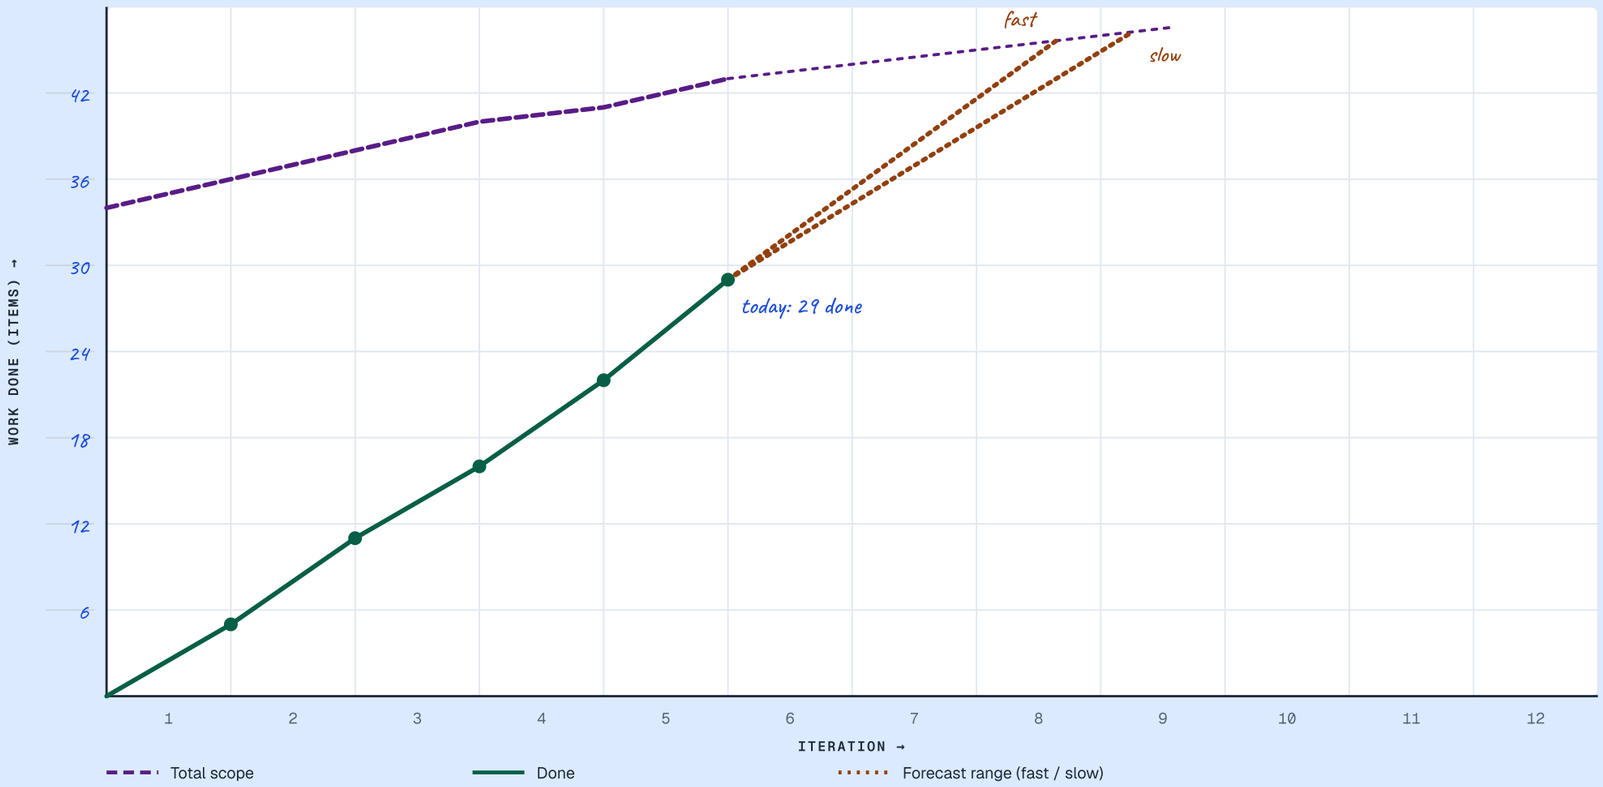

2 Throughput Data

ITEMS FINISHED PER ITERATION

ITERATION	DONE	ADDED	TOTAL SCOPE
1	5	–	36
2	6	2	38
3	5	2	40
4	6	1	41
5	7	2	43

Average per iteration: 5.8

Slowest 3, average: 5.3

Fastest 3, average: 6.3

3 The Forecast

REMAINING / RATE = ITERATIONS LEFT

Remaining items (incl. expected growth): 16 (14 + 2 growth)

SCENARIO	RATE / ITERATION	ITERATIONS LEFT	DATE
Slow	5.3	3.0	20 June
Likely	5.8	2.8	18 June
Fast	6.3	2.5	13 June

4 What Would Change It

UPDATE THE FORECAST WHEN THESE MOVE

- Scope growth · team changes · dependencies · item size changing
- Share the range and the assumptions, not just the likely date

Splitting substitutes added 3 items

Stock API late: could stall substitutes

Ravi up to speed: more throughput

Next forecast update: every Friday, after the review

“When will it be done? Here's the range, and here's what it depends on.”

“What would have to be true for the fast forecast to happen?”

© 2026 Eric Parker · CC BY 4.0 · eparker71.github.io/better-delivery-toolkit
