Release Forecast & Burn-up

Answer “when will it be done?” with a range, based on how fast the team actually finishes work.


Run a Project · Burn-up Chart · Throughput Forecasting · Ranges, Not Single Dates

RELEASE / SCOPE _____

FORECAST DATE _____

1 Burn-up Chart

PLOT AFTER EVERY ITERATION

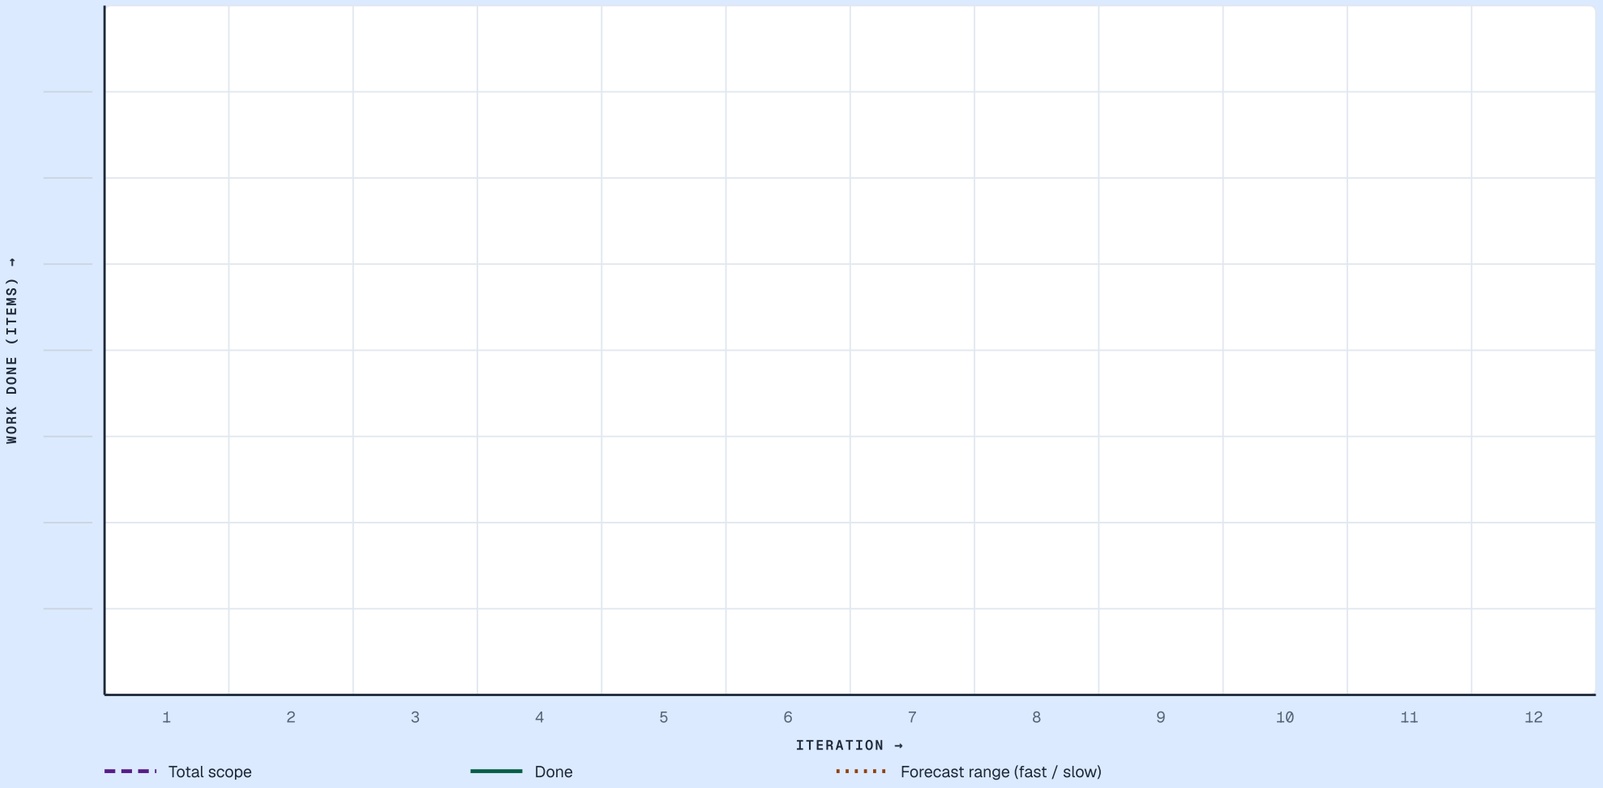

2 Throughput Data

ITEMS FINISHED PER ITERATION

ITERATION	DONE	ADDED	TOTAL SCOPE

Average per iteration: _____

Slowest 3, average: _____

Fastest 3, average: _____

3 The Forecast

REMAINING / RATE = ITERATIONS LEFT

Remaining items (incl. expected growth): _____

SCENARIO	RATE / ITERATION	ITERATIONS LEFT	DATE
Slow			
Likely			
Fast			

4 What Would Change It

UPDATE THE FORECAST WHEN THESE MOVE

- Scope growth · team changes · dependencies · item size changing
- Share the range and the assumptions, not just the likely date

Add your sticky notes here

Next forecast update: _____

“When will it be done? Here's the range, and here's what it depends on.”

“What would have to be true for the fast forecast to happen?”

© 2026 Eric Parker · CC BY 4.0 · eparker71.github.io/better-delivery-toolkit
